

BRHAT BANGALORE MAHANAGARA PALIKE
INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roads and Drains at Chaokkanahalli Circle to Nanjareddy's House in Ward No. 05 Byatarayanapura Sub Division	
2	Estimate Cost	45.00 Lakhs	
3	Administrative Approved No and Date	617/13-14, Date. 23.12.2013	
4	Technical sanction No. and Date	60/13-14, 23.12.2013	
5	Job Code No. and P Code No.	005-14-000032	
6	Tender Direct Entrested to KRIDL	KRIDL	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable	
8	Tender Approved Details	Not Applicable	
9	Work Order No and Date	371/13-14, Date. 21.02.2014	
10	Stipulation time of Completion	90 Days	
11	Actual Date of Commencement	21.02.2014	
12	Actual Date of Completion	28.07.2014	
13	Delay if any	Nil	

14	Reason for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verified	Enclosed	
18	Date of Inspection	12.01.2016	
19	MB No. and Page No.	Mb No.2503 Page No. 250223-238	
20	BR No. and Date	210/31.07.2014	
21	Test Result	Quality Test Report submitted by Civil Tech Consultants and Engineers is verified and Enclosed	
22	Section officer	Sri P A Chandrakanthraju A.E	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
a	Work Quality	Satisfactory	
b	Comments	Work completed as per MB	


 ಸಹಾಯಕ ಅಭಿಯಂತರರು
 ಜ್ಞಾಪರಾಯನಪುರ ಉಪ ವಿಭಾಗ



 12/1/16

Name of work :- Improvements to Roads & Drains at Chokkanahally
Circle to Nanja Reddy's house in ward NO-5 of Gyr-Susubini.




AE-05
ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಿಯನಪುರ ಉಪ ವಿಭಾಗ

— 2 —

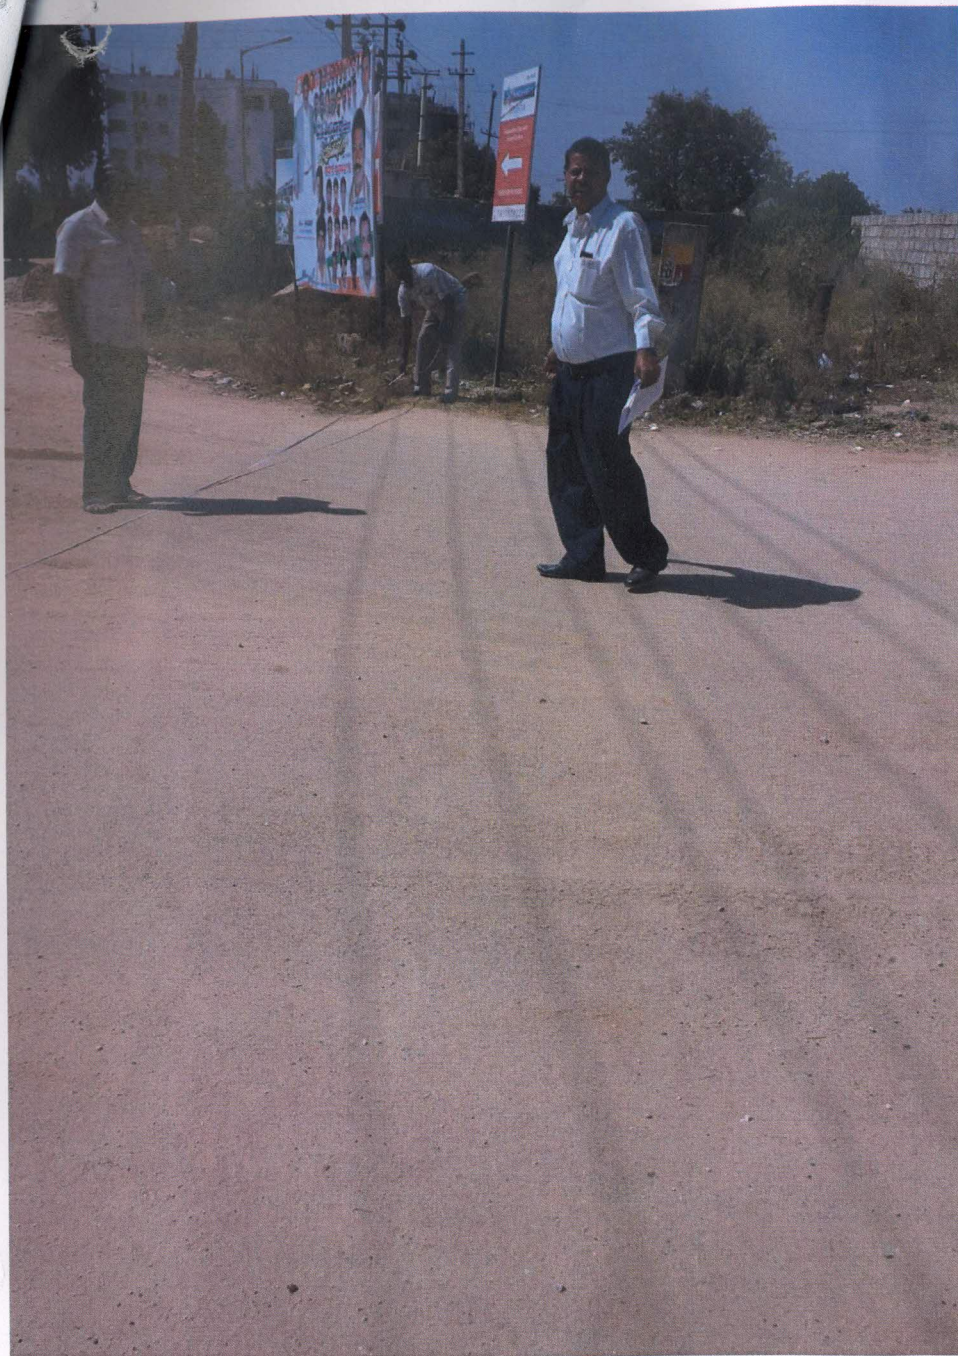


Qp
FAE-01

24-7

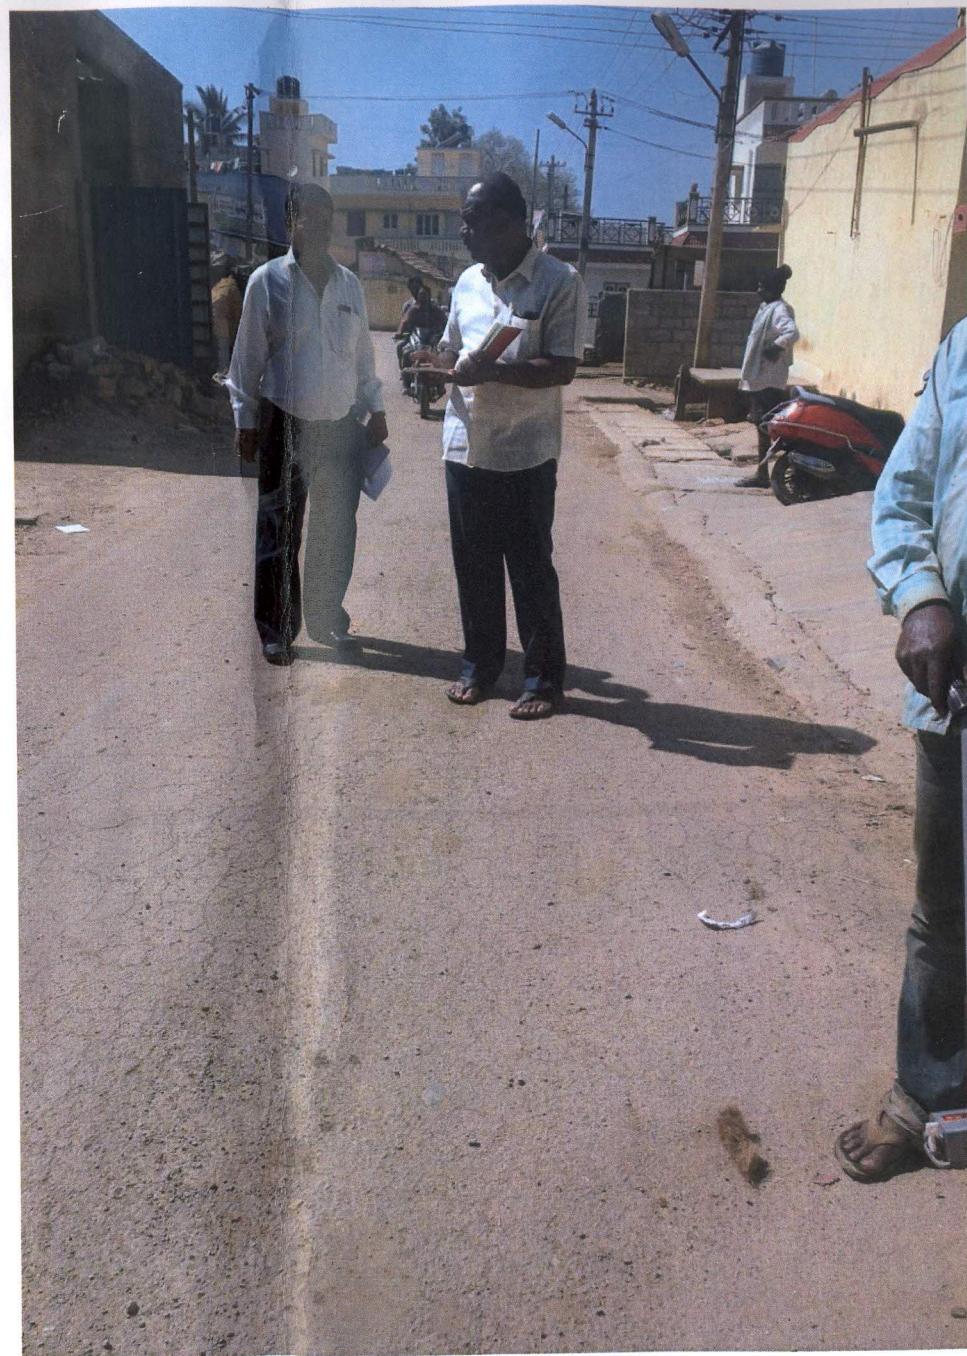

happ

10
85
... Roads & Drains at Chokkanahally
... No-5 of Byr-Sus-din.

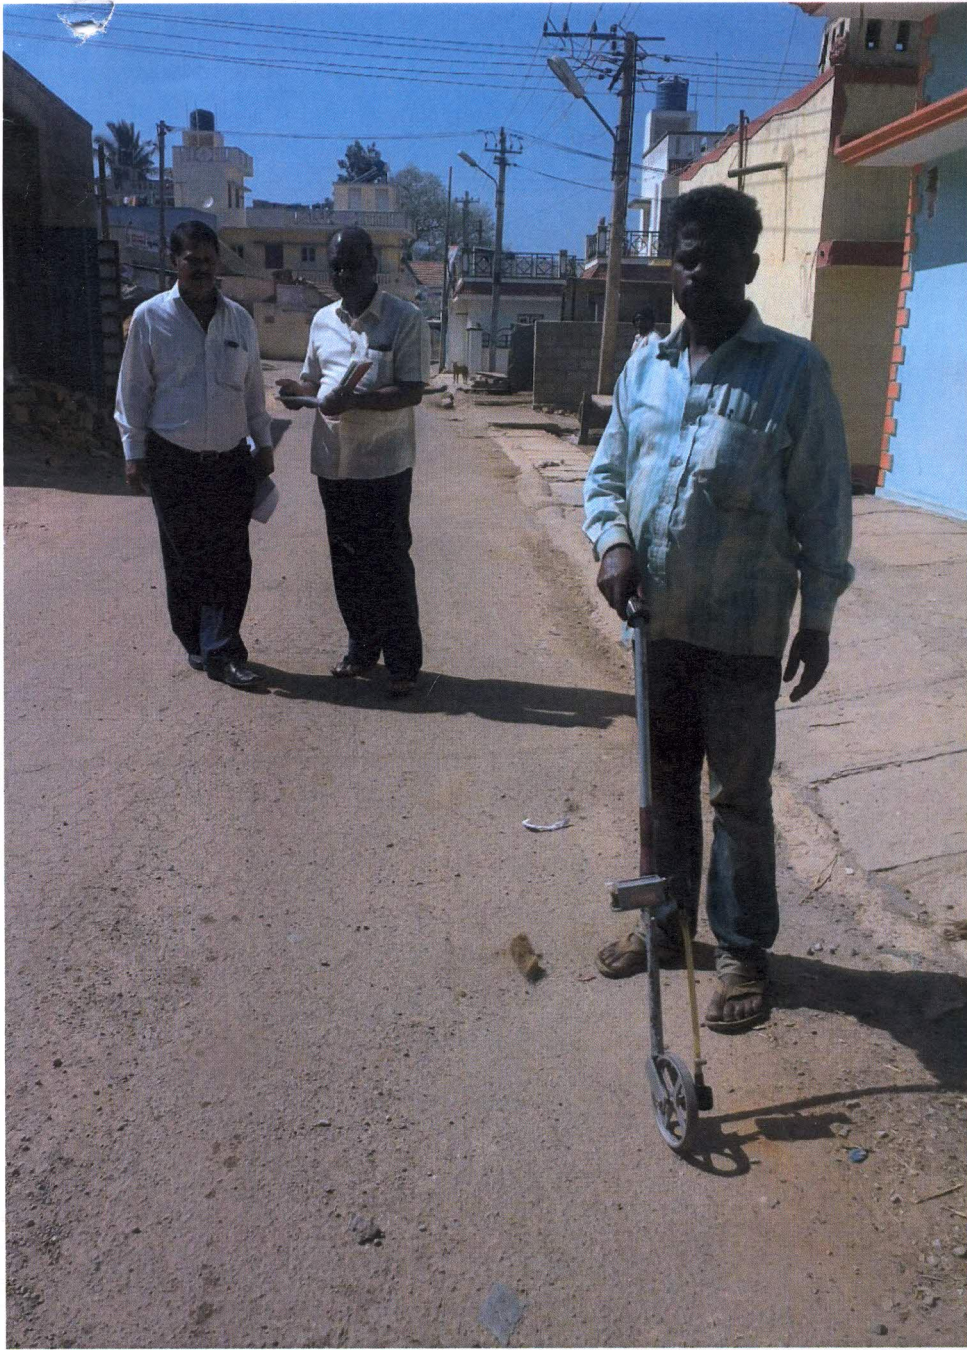

Byr AE-05

7

Byr AE-05
ಸಹಾಯಕ ಅಭಿಯಂತರರು
ವಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಿಯನಪುರ ಉಪ ವಿಭಾಗ

7
